

Region	Study Cycle	Number of Projects	MW's	DPP Start	DPP 1 Completion	DPP 2 Completion	DPP 3 Completion	GIA Execution	Current Stage/Status	Reason for Delay	Expected Time of Delay	Details
Central	DPP-2016-FEB	3	1,307	8/15/2016		12/15/2016	3/15/2017	1/18/2018	GIA Complete			
	DPP-2016-AUG	7	1,019	1/5/2017	6/22/2017		1/17/2018	5/24/2018	11/1/2018	GIA Complete		
	DPP-2017-FEB	10	2,354	6/22/2017	5/31/2018	9/18/2018	5/20/2019	10/17/2019	NU FS In Progress	TO Delay		NU FAS delayed due to need to perform structural analysis for possible rebuilding 1.5 miles of 69 kV
	DPP-2017-AUG	28	4,630	6/1/2018	1/8/2019	4/17/2019	8/29/2019	1/27/2020	DPP 3	TO Delay		Affected System and TO Stability Final reports were late.
	DPP-2018-APR	48	9,223	4/22/2019	9/11/2019	12/4/2019	4/16/2020	9/14/2020	DPP 1	Pending Previous Study Results		DPP-2017-AUG DPP 2 Completion delayed
DPP-2019-Cycle 1	TBD	TBD	12/5/2019	4/24/2020	7/14/2020	11/25/2020	4/26/2021					
East (ATC)	DPP-2016-FEB	1	99	12/13/2016	5/2/2017	7/14/2017	9/8/2017	1/22/2018	GIA Complete			
	DPP-2016-AUG	1	98	5/2/2017	9/6/2017	1/16/2018	5/31/2018	10/28/2018	GIA Complete			GIA's are complete
	DPP-2017-FEB	2	90	10/20/2017	4/10/2018	9/20/2018	10/5/2018	3/29/2019	GIA Complete			GIA's are complete
	DPP-2017-AUG	14	2,208	4/13/2018	1/8/2019	4/12/2019	8/26/2019	1/23/2020	DPP 3	Affected System Study Delay		Delay in receiving PJM Affected System Study.
	DPP-2018-APR	23	3,610	4/23/2019	9/12/2019	12/4/2019	4/16/2020	9/14/2020	DPP 1	MISO Delay		Kick-off calls delayed due to schedule conflicts.
DPP-2019-Cycle 1	TBD	TBD	12/5/2019	4/24/2020	7/14/2020	11/25/2020	4/26/2021					
East (ITC)	DPP-2016-FEB	3	399	2/24/2017	7/28/2017	12/21/2017	5/5/2018	10/2/2018	GIA Complete			
	DPP-2016-AUG	3	355	2/24/2017	8/21/2017	1/16/2018	9/5/2018	2/4/2019	GIA Complete			GIA's are complete
	DPP-2017-FEB	5	702	10/13/2017	5/2/2018	9/6/2018	4/26/2019	9/23/2019	GIA In Progress	Affected System Study Delay		Delay in Network Upgrade Facilities study
	DPP-2017-AUG	14	3,697	5/3/2018	1/9/2019	4/23/2019	9/4/2019	2/3/2020	DPP 3	Affected System Study Delay		Delay in Affected System Study
	DPP-2018-APR	25	3,719	5/1/2019	9/20/2019	12/10/2019	4/22/2020	9/21/2020	DPP 1	MISO Delay		Kick-off calls delayed due to schedule conflicts.
	DPP-2019-Cycle 1	TBD	TBD	12/11/2019	4/30/2020	7/21/2020	12/2/2020	5/3/2021				
East (UP)	DPP-2016 AUG / 2017-FEB	2	183	2/6/2017	2/26/2017	8/8/2017	10/25/2017	3/24/2018	GIA Complete			GIA and MPFCA completed for all 3 projects.
	DPP-2017-AUG	2	205	12/21/2017	5/22/2018	9/11/2018	2/21/2019	7/22/2019	GIA In Progress			All projects are in GIA phase
South	DPP-2016-AUG	13	2,917	10/3/2016	5/16/2017	8/8/2017	12/21/2017	7/13/2018	GIA Complete			
	DPP-2017-FEB	3	250	2/8/2017	6/28/2017	2/13/2018	5/14/2018	10/11/2018	GIA Complete			GIA's are complete
	DPP-2017-AUG	15	1,842	2/14/2018	1/8/2019	3/25/2019	8/6/2019	1/3/2020	DPP 3			Finished SIS Report 1 week early – moving up start of decision point.
	DPP-2018-APR	44	7,818	3/27/2019	8/15/2019	11/5/2019	3/19/2020	8/17/2020	DPP 1			DPP-2017-AUG-South finished 1 week early. Moving up start of this cycle 1 week.
DPP-2019-Cycle 1	TBD	TBD	11/13/2019	4/2/2020	6/22/2020	11/4/2020	4/5/2021					
West	DPP-2016-FEB	24	4,783	1/27/2017	8/31/2017	3/26/2018	9/24/2018	3/29/2019	GIA Complete			GIA's are complete
	DPP-2016-AUG	13	2,302	9/12/2017	10/12/2018	1/15/2019	6/11/2019	11/8/2019	DPP 3	Model/Mitigation Delay		3 additional constraints caused by the proposed network upgrades occurred and needed
	DPP-2017-FEB	12	1,395	10/15/2018	4/9/2019	7/1/2019	11/13/2019	4/13/2020	DPP 2	IC Delay		Waited for modeling data from IC.
	DPP-2017-AUG	36	5,482	6/12/2019	11/1/2019	1/24/2020	6/8/2020	11/5/2020				Based on the experience with the last two cycles, MISO has decided to push the start date of Aug-2017-West cycle to June so that it can use latest project and upgrade information from Feb 2017 West cycle in Phase 1 studies.
	DPP-2018-APR	62	9,483	1/27/2020	6/16/2020	9/4/2020	1/19/2021	6/18/2021				
DPP-2019-Cycle 1	TBD	TBD	9/8/2020	1/28/2021	4/19/2021	8/31/2021	1/28/2022					

- Notes:**
- 1) The dates provided are an estimate of queue cycle performance (including Federal Holidays or Weekends).
  - 2) The dates provided are inclusive of the associated Decision Points. Final study reports are posted 15 business days prior to the completion dates.
  - 3) DPP3 (Final System Impact Study) of several DPP cycles is scheduled to start before expected GIA execution of higher queued cycles. This schedule does not consider any restudies that may occur after Decision Point 2 of higher queued cycles.
  - 4) Updates from the previous version are provided in red font.
  - 5) The number of projects or MWs in a study group may change throughout the study process.

- Categories for Reason of Delay:**
- TO Delay
  - MISO Delay
  - IC Delay
  - Restudy Delay
  - Affected System Study Delay
  - Pending FERC Ruling
  - Model/Mitigation Delay
  - Pending Previous Study Results

Federal Holiday	2019	2020
News Year's Day	1/1/2019	1/1/2020
Martin Luther King Day	1/21/2019	1/20/2020
Presidents' Day	2/18/2019	2/17/2020
Memorial Day	5/27/2019	5/25/2020
Independence Day	7/4/2019	7/3/2020
Labor Day	9/2/2019	9/7/2020
Columbus Day	10/14/2019	10/12/2020
Veterans Day	11/11/2019	11/11/2020
Thanksgiving Day	11/28/2019	11/26/2020
Christmas Day	12/25/2019	12/25/2020

Region	Study Cycle	Number of Projects	MWs	DPP Start	DPP 1 Completion	DPP 2 Completion	DPP 3 Completion	GIA Execution	Current Stage/Status	Reason for Delay	Expected Time of Delay	Details
Central	DPP-2016-FEB	3	1,307	8/15/2016		12/15/2016	3/15/2017	1/18/2018	GIA Complete			
	DPP-2016-AUG	7	1,019	1/5/2017	6/22/2017	1/17/2018	5/24/2018	11/1/2018	GIA Complete			
	DPP-2017-FEB	10	2,354	6/22/2017	5/31/2018	9/18/2018	5/20/2019	10/17/2019	NU FS In Progress	TO Delay		NU FAS delayed due to need to perform structural analysis for possible rebuilding 1.5 miles of 69 kV
	DPP-2017-AUG	32	5,475	6/1/2018	1/8/2019	4/17/2019	8/29/2019	1/27/2020	DPP 2	TO Delay		Affected System and TO Stability Final reports were late.
	DPP-2018-APR	49	9,323	4/22/2019	9/11/2019	12/4/2019	4/16/2020	9/14/2020		Pending Previous Study Results		DPP-2017-AUG DPP 2 Completion delayed
DPP-2019-Cycle 1	TBD	TBD	12/5/2019	4/24/2020	7/14/2020	11/25/2020	4/26/2021					
East (ATC)	DPP-2016-FEB	1	99	12/13/2016	5/2/2017	7/14/2017	9/8/2017	1/22/2018	GIA Complete			
	DPP-2016-AUG	1	98	5/2/2017	9/6/2017	1/16/2018	5/31/2018	10/28/2018	GIA Complete			GIA's are complete
	DPP-2017-FEB	2	90	10/20/2017	4/10/2018	9/20/2018	10/5/2018	3/29/2019	GIA Complete			GIA's are complete
	DPP-2017-AUG	14	2,208	4/13/2018	1/8/2019	4/12/2019	8/26/2019	1/23/2020	DPP 2	Affected System Study Delay		Delay in receiving PJM Affected System Study.
	DPP-2018-APR	23	3,610	4/15/2019	9/4/2019	11/26/2019	4/9/2020	9/8/2020		Pending Previous Study Results		
DPP-2019-Cycle 1	TBD	TBD	11/27/2019	4/16/2020	7/7/2020	11/18/2020	4/19/2021					
East (ITC)	DPP-2016-FEB	3	399	2/24/2017	7/28/2017	12/21/2017	5/5/2018	10/2/2018	GIA Complete			
	DPP-2016-AUG	3	355	2/24/2017	8/21/2017	1/16/2018	9/5/2018	2/4/2019	GIA Complete			GIA's are complete
	DPP-2017-FEB	5	702	10/13/2017	5/2/2018	9/6/2018	4/5/2019	9/3/2019	NU FS In Progress	TO Delay		Delay in receiving NU FaS from TO
	DPP-2017-AUG	16	3,994	5/3/2018	1/9/2019	4/19/2019	9/3/2019	1/31/2020	DPP 2	Stability Results Delay		Stability Model and PJM Affected System Study took more time than expected.
	DPP-2018-APR	28	4,149	4/22/2019	9/11/2019	12/4/2019	4/16/2020	9/14/2020		Pending Previous Study Results		
DPP-2019-Cycle 1	TBD	TBD	12/5/2019	4/24/2020	7/14/2020	11/25/2020	4/26/2021					
East (UP)	DPP-2016 AUG / 2017-FEB	0	0	2/6/2017	2/26/2017	8/8/2017	10/25/2017	3/24/2018	GIA Complete			GIA and MPFCA completed for all 3 projects.
	DPP-2017-AUG	2	205	12/21/2017	5/22/2018	9/11/2018	2/21/2019	7/22/2019	GIA In Progress			All projects are in GIA phase
South	DPP-2016-AUG	13	2,917	10/3/2016	5/16/2017	8/8/2017	12/21/2017	7/13/2018	GIA Complete			
	DPP-2017-FEB	4	350	2/8/2017	6/28/2017	2/13/2018	5/14/2018	10/11/2018	GIA Complete			GIA's are complete
	DPP-2017-AUG	15	1,842	2/14/2018	1/8/2019	3/25/2019	8/6/2019	1/3/2020	DPP 3			Finished SIS Report 1 week early – moving up start of decision point.
	DPP-2018-APR	44	7,828	3/27/2019	8/15/2019	11/5/2019	3/19/2020	8/17/2020	DPP 1			DPP-2017-AUG-South finished 1 week early. Moving up start of this cycle 1 week.
DPP-2019-Cycle 1	TBD	TBD	11/13/2019	4/2/2020	6/22/2020	11/4/2020	4/5/2021					
West	DPP-2016-FEB	24	4,783	1/27/2017	8/31/2017	3/26/2018	9/24/2018	3/29/2019	GIA Complete			GIA's are complete
	DPP-2016-AUG	13	2,302	9/12/2017	10/12/2018	1/15/2019	6/11/2019	11/8/2019	DPP 3	Model/Mitigation Delay		3 additional constraints caused by the proposed network upgrades occurred and needed
	DPP-2017-FEB	27	3,423	10/15/2018	4/9/2019	6/28/2019	11/12/2019	4/10/2020	DPP 1	Model/Mitigation Delay		Multiple rounds of mitigation identification and justification required due to the volume and complexity of the study has caused delay in the completion of DPP Phase 1.
	DPP-2017-AUG	36	5,490	6/12/2019	11/1/2019	1/24/2020	6/8/2020	11/5/2020				Based on the experience with the last two cycles, MISO has decided to push the start date of Aug-2017-West cycle to June so that it can use latest project and upgrade information from Feb 2017 West cycle in Phase 1 studies.
	DPP-2018-APR	65	10,383	1/27/2020	6/16/2020	9/4/2020	1/19/2021	6/18/2021				
DPP-2019-Cycle 1	TBD	TBD	9/8/2020	1/28/2021	4/19/2021	8/31/2021	1/28/2022					

**Notes:**


- 1) The dates provided are an estimate of queue cycle performance (including Federal Holidays or Weekends).
- 2) The dates provided are inclusive of the associated Decision Points. Final study reports are posted 15 business days prior to the completion dates.
- 3) DPP3 (Final System Impact Study) of several DPP cycles is scheduled to start before expected GIA execution of higher queued cycles. This schedule does not consider any restudies that may occur after Decision Point 2 of higher queued cycles.
- 4) Updates from the previous version are provided in red font.
- 5) The number of projects or MWs in a study group may change throughout the study process.

**Categories for Reason of Delay:**

- TO Delay
- MISO Delay
- IC Delay
- Restudy Delay
- Affected System Study Delay
- Pending FERC Ruling
- Model/Mitigation Delay
- Pending Previous Study Results

Federal Holiday	2019	2020
News Year's Day	1/1/2019	1/1/2020
Martin Luther King Day	1/21/2019	1/20/2020
Presidents' Day	2/18/2019	2/17/2020
Memorial Day	5/27/2019	5/25/2020
Independence Day	7/4/2019	7/3/2020
Labor Day	9/2/2019	9/7/2020
Columbus Day	10/14/2019	10/12/2020
Veterans Day	11/11/2019	11/11/2020
Thanksgiving Day	11/28/2019	11/26/2020
Christmas Day	12/25/2019	12/25/2020

# Generator Interconnection Process

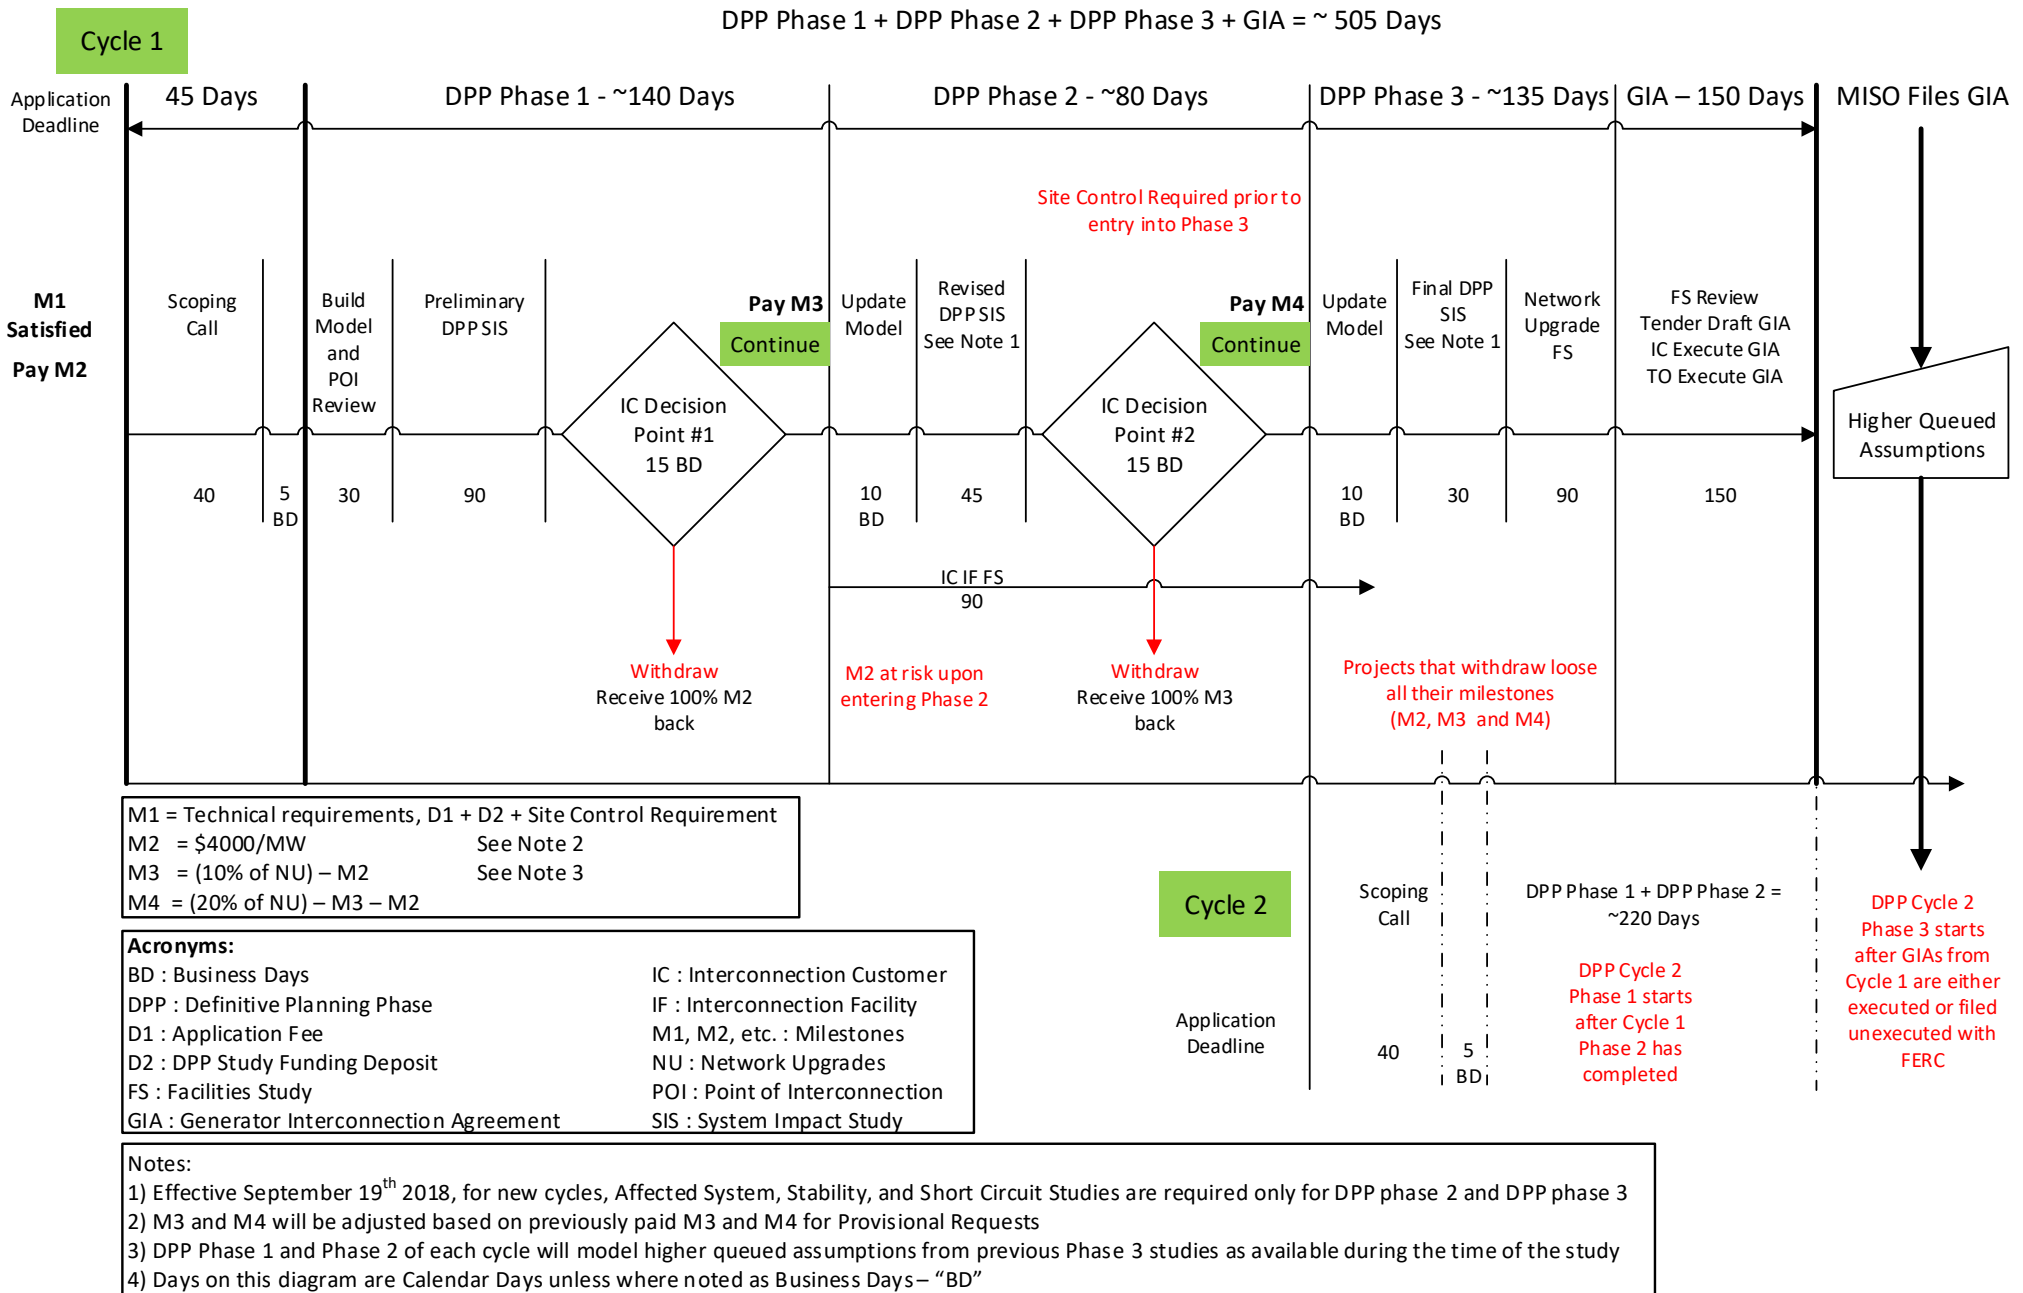

Refer to full GI Process Flow Diagram and notes for more detail: [GI Application and DPP Readiness](#)
