

Region	Study Cycle	Number of Projects	MWs	Site Control Date	DPP 1 Start	DPP 1 Completion	DPP 2 Completion	DPP 3 Completion	GIA Execution	Current Stage/Status	Reason for Delay	Expected Time of Delay	Details
Central	DPP-2018-APR	35	7,544		4/22/2019	1/7/2020	3/10/2021	12/30/2021	5/31/2022	DPP 3	TO Delay		TO LPC results took longer to mitigate due to size of Queue
	DPP-2019-Cycle	81	13,216		6/23/2020	8/5/2021	12/14/2021	4/27/2022	9/28/2022	DPP 1	Model/Mitigation Delay		IC Model Correction Delay
	DPP-2020-Cycle	85	13,173		3/15/2021	12/6/2021	2/25/2022	7/11/2022	12/8/2022	DPP 1	MISO Delay		Model building delay
	DPP-2021-Cycle	144	22,019		10/20/2021	3/11/2022	5/31/2022	10/12/2022	3/13/2023				
	DPP-2022-Cycle	-	-	9/15/2022	12/14/2022	5/4/2023	7/25/2023	12/6/2023	5/6/2024				
East (ATC)	DPP-2018-APR	11	945		4/23/2019	10/25/2019	5/19/2020	5/7/2021	10/4/2021	GIA In Progress	Affected System Study Delay		Network Upgrade Facilities studies final reports expected by first week of May
	DPP-2019-Cycle	16	1,721		5/20/2020	2/11/2021	11/22/2021	4/6/2022	9/6/2022	DPP 2	Affected System Study Delay		PJM Affected System Study not expected until mid-October
	DPP-2020-Cycle	29	3,850		2/24/2021	7/30/2021	11/15/2021	3/30/2022	8/29/2022	DPP 1	IC Delay		Resolving stability model issues with certain IC's
	DPP-2021-Cycle	40	5,601		10/20/2021	3/11/2022	5/31/2022	10/12/2022	3/13/2023				
	DPP-2022-Cycle	-	-	9/15/2022	12/14/2022	5/4/2023	7/25/2023	12/6/2023	5/6/2024				
East (ITC)	DPP-2018-APR	6	1,004		5/1/2019	12/2/2019	6/30/2020	3/26/2021	8/23/2021	GIA In Progress	Affected System Study Delay		GIA Negotiations underway
	DPP-2019-Cycle	28	3,621		7/7/2020	2/11/2021	11/22/2021	4/6/2022	9/6/2022	DPP 2	Affected System Study Delay		PJM Affected System Study not expected until mid-October
	DPP-2020-Cycle	29	4,947		2/24/2021	12/28/2021	3/21/2022	8/2/2022	12/30/2022	DPP 1	IC Delay		IC used cure period to submit A10 Model Review forms after deadline
	DPP-2021-Cycle	60	9,782		10/20/2021	3/11/2022	5/31/2022	10/12/2022	3/13/2023				
	DPP-2022-Cycle	-	-	9/15/2022	12/14/2022	5/4/2023	7/25/2023	12/6/2023	5/6/2024				
South	DPP-2018-APR	12	1,681		3/27/2019	8/29/2019	1/24/2020	7/1/2020	12/31/2020	GIA In Progress			All projects except one have a completed GIA
	DPP-2019-Cycle	34	5,545		2/10/2020	8/6/2020	3/18/2021	1/27/2022	6/27/2022	DPP 3	Affected System Study Delay		TVA Affected System Delay
	DPP-2020-Cycle	64	8,850		12/22/2020	10/20/2021	1/11/2022	5/26/2022	10/24/2022	DPP 1	MISO/TO Delay		Delay due to large number of projects and the complexity of solution development
	DPP-2021-Cycle	150	25,793		10/20/2021	3/11/2022	5/31/2022	10/12/2022	3/13/2023				
	DPP-2022-Cycle	-	-	9/15/2022	12/14/2022	5/4/2023	7/25/2023	12/6/2023	5/6/2024				
West	DPP-2017-AUG	11	1,808		6/12/2019	10/24/2019	2/1/2021	8/16/2021	1/13/2022	GIA In Progress			All but one project engaged in GIA negotiations
	DPP-2018-APR	20	2,317		9/9/2019	3/25/2020	3/9/2021	9/13/2021	12/15/2021	GIA In Progress			Four projects engaged in GIA negotiations.
	DPP-2019-Cycle	36	5,883		5/5/2020	3/19/2021	11/22/2021	4/6/2022	9/6/2022	DPP 2	Affected System Study Delay		Final version of SIS pending PJM and Minnkota AFS studies
	DPP-2020-Cycle	41	5,472		1/6/2021	11/5/2021	1/28/2022	6/13/2022	11/10/2022	DPP 1	MISO/TO Delay		Waiting on LPC reports to incorporate into the draft System Impact Study
	DPP-2021-Cycle	73	11,635		10/20/2021	3/11/2022	5/31/2022	10/12/2022	3/13/2023				
	DPP-2022-Cycle	-	-	9/15/2022	12/14/2022	5/4/2023	7/25/2023	12/6/2023	5/6/2024				

Notes:

- 1) The dates provided are an estimate of queue cycle performance (including Federal Holidays or Weekends).
- 2) The dates provided are inclusive of the associated Decision Points. Final study reports are posted 15 business days prior to the completion dates.
- 3) DPP3 (Final System Impact Study) of several DPP cycles is scheduled to start before expected GIA execution of higher queued cycles. This schedule does not consider any restudies that may occur after Decision Point 2 of higher queued cycles.
- 4) Updates from the previous version are provided in red font.
- 5) The number of projects or MWs in a study group may change throughout the study process.

Categories for Reason of Delay:

- TO Delay
- MISO Delay
- MISO Delay/TO Delay
- IC Delay
- Restudy Delay
- Affected System Study Delay
- Pending FERC Ruling
- Model/Mitigation Delay
- Pending Previous Study Results

Federal Holiday	2021	2022
News Year's Day	1/1/2021	12/31/2021
Martin Luther King Day	1/18/2021	1/17/2022
Presidents' Day	2/15/2021	2/21/2022
Memorial Day	5/31/2021	5/30/2022
Independence Day	7/5/2021	7/4/2022
Labor Day	9/6/2021	9/5/2022
Columbus Day	10/11/2021	10/10/2022
Veterans Day	11/11/2021	11/11/2022
Thanksgiving Day	11/25/2021	11/24/2022
Christmas Day	12/24/2021	12/26/2022

Region	Study Cycle	Number of Projects	MWs	DPP 1 Start	DPP 1 Completion	DPP 2 Completion	DPP3 Planned Completion Dates		DPP 3 Completion	GIA Execution	Current Stage/Status	Reason for Delay	Expected Time of Delay	Details
							DPP3 SIS Date							
Central	DPP-2018-APR	35	7,544	4/22/2019	1/7/2020	3/10/2021	9/29/2021	12/28/2021	5/27/2022	DPP 3	Affected System Study Delay		TVA Affected System Study Delay	
	DPP-2019-Cycle	81	13,216	6/23/2020	8/5/2021	11/23/2021	1/7/2022	4/7/2022	9/6/2022	DPP 1	Model/Mitigation Delay		IC DP1 Breach Delay	
	DPP-2020-Cycle	85	13,173	3/15/2021	12/6/2021	2/25/2022	4/10/2022	7/11/2022	12/8/2022	DPP 1	MISO Delay		Model building delay	
	DPP-2021-Cycle	-	-	10/20/2021	3/11/2022	5/31/2022	7/14/2022	10/12/2022	3/13/2023					
East (ATC)	DPP-2018-APR	11	945	4/23/2019	10/25/2019	5/19/2020		5/7/2021	10/4/2021	GIA In Progress			All projects now in GIA Negotiations	
	DPP-2019-Cycle	16	1,721	5/20/2020	2/11/2021	11/1/2021	12/16/2021	3/16/2022	8/15/2022	DPP 2	Affected System Study Delay		PJM Affected System Study not expected until September	
	DPP-2020-Cycle	29	3,850	2/24/2021	7/30/2021	11/1/2021	12/16/2021	3/16/2022	8/15/2022	DPP 1	MISO Delay		Administrative delay following model review period	
	DPP-2021-Cycle	-	-	10/20/2021	3/11/2022	5/31/2022	7/14/2022	10/12/2022	3/13/2023					
East (ITC)	DPP-2018-APR	6	1,004	5/11/2019	12/2/2019	6/30/2020		3/26/2021	8/23/2021	GIA In Progress			GIA Negotiations underway	
	DPP-2019-Cycle	28	3,621	7/7/2020	2/11/2021	11/1/2021	12/16/2021	3/16/2022	8/15/2022	DPP 2	Affected System Study Delay		PJM Affected System Study not expected until September	
	DPP-2020-Cycle	29	4,947	2/24/2021	12/28/2021	3/21/2022	5/4/2022	8/2/2022	12/30/2022	DPP 1	IC Delay		IC used cure period to submit A10 Model Review forms after deadline	
	DPP-2021-Cycle	2	200	10/20/2021	3/11/2022	5/31/2022	7/14/2022	10/12/2022	3/13/2023					
South	DPP-2018-APR	12	1,681	3/27/2019	8/29/2019	1/24/2020		7/1/2020	12/31/2020	GIA In Progress			All projects except one have a completed GIA	
	DPP-2019-Cycle	34	5,545	2/10/2020	8/6/2020	3/18/2021	10/29/2021	1/27/2022	6/27/2022	DPP 3	Affected System Study Delay		TVA Affected System Delay	
	DPP-2020-Cycle	64	8,850	12/22/2020	10/4/2021	12/24/2021	2/9/2022	5/10/2022	10/7/2022	DPP 1	MISO/TO Delay		Delay due to large number of projects and the complexity of solution development	
	DPP-2021-Cycle	-	-	10/20/2021	3/11/2022	5/31/2022	7/14/2022	10/12/2022	3/13/2023					
West	DPP-2017-AUG	11	1,808	6/12/2019	10/24/2019	2/1/2021		8/16/2021	1/13/2022	GIA In Progress				
	DPP-2018-APR	20	2,317	9/9/2019	3/25/2020	3/9/2021		9/13/2021	12/15/2021	GIA In Progress				
	DPP-2019-Cycle	36	5,883	5/5/2020	3/19/2021	10/22/2021	12/5/2021	3/7/2022	8/4/2022	DPP 2	Affected System Study Delay		Final version of System Impact study pending PJM and Minnesota AFS studies.	
	DPP-2020-Cycle	41	5,472	1/6/2021	10/20/2021	1/11/2022	2/25/2022	5/26/2022	10/24/2022	DPP 1	MISO/TO Delay		Change in schedule of 28 days due to delayed LPC study results	
DPP-2021-Cycle	-	-	10/20/2021	3/11/2022	5/31/2022	7/14/2022	10/12/2022	3/13/2023						


Notes:

- 1) The dates provided are an estimate of queue cycle performance (including Federal Holidays or Weekends).
- 2) The dates provided are inclusive of the associated Decision Points. Final study reports are posted 15 business days prior to the completion dates.
- 3) DPP3 (Final System Impact Study) of several DPP cycles is scheduled to start before expected GIA execution of higher queued cycles. This schedule does not consider any restudies that may occur after Decision Point 2 of higher queued cycles.
- 4) Updates from the previous version are provided in red font.
- 5) The number of projects or MWs in a study group may change throughout the study process.

Categories for Reason of Delay:


- TO Delay
- MISO Delay
- MISO Delay/TO Delay
- IC Delay
- Restudy Delay
- Affected System Study Delay
- Pending FERC Ruling
- Model/Mitigation Delay
- Pending Previous Study Results

Federal Holiday	2021	2022
News Year's Day	1/1/2021	12/31/2021
Martin Luther King Day	1/18/2021	1/17/2022
Presidents' Day	2/15/2021	2/21/2022
Memorial Day	5/31/2021	5/30/2022
Independence Day	7/5/2021	7/4/2022
Labor Day	9/6/2021	9/5/2022
Columbus Day	10/11/2021	10/10/2022
Veterans Day	11/11/2021	11/11/2022
Thanksgiving Day	11/25/2021	11/24/2022
Christmas Day	12/24/2021	12/26/2022

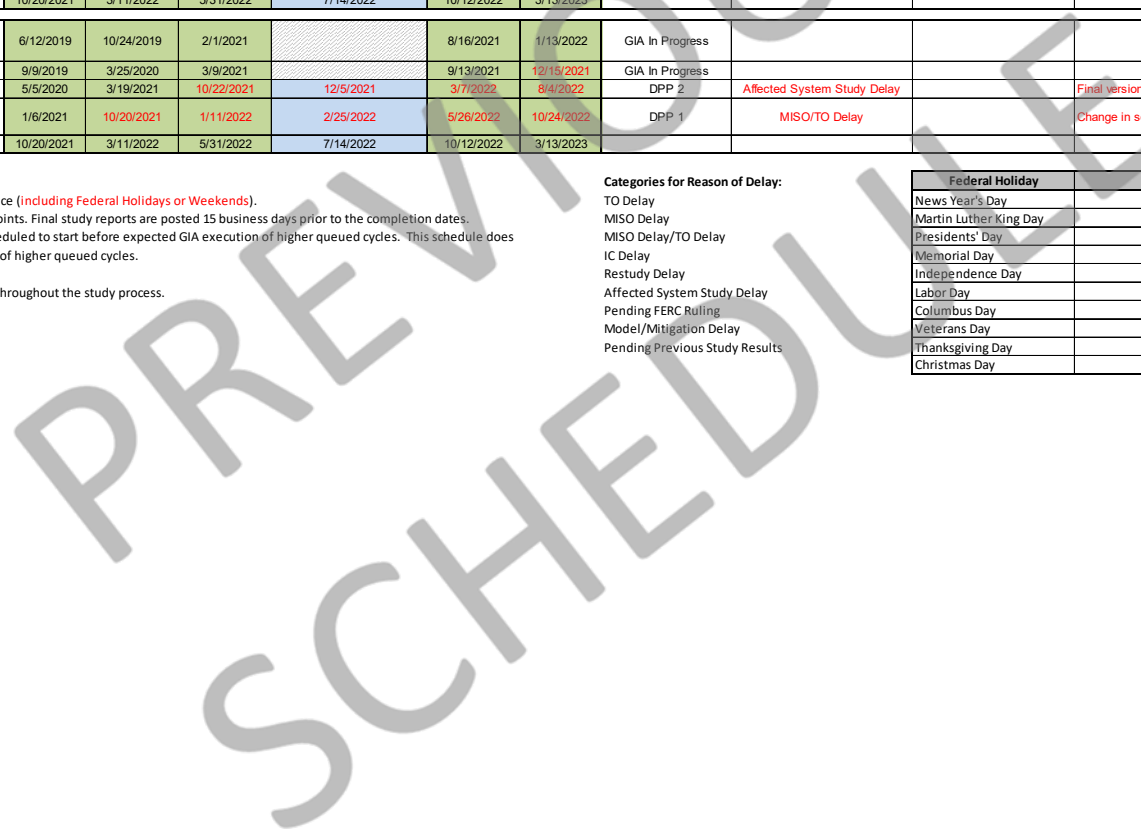

Generator Interconnection Process

DPP Phase 1 + DPP Phase 2 + DPP Phase 3 + GIA = ~ 505 Days

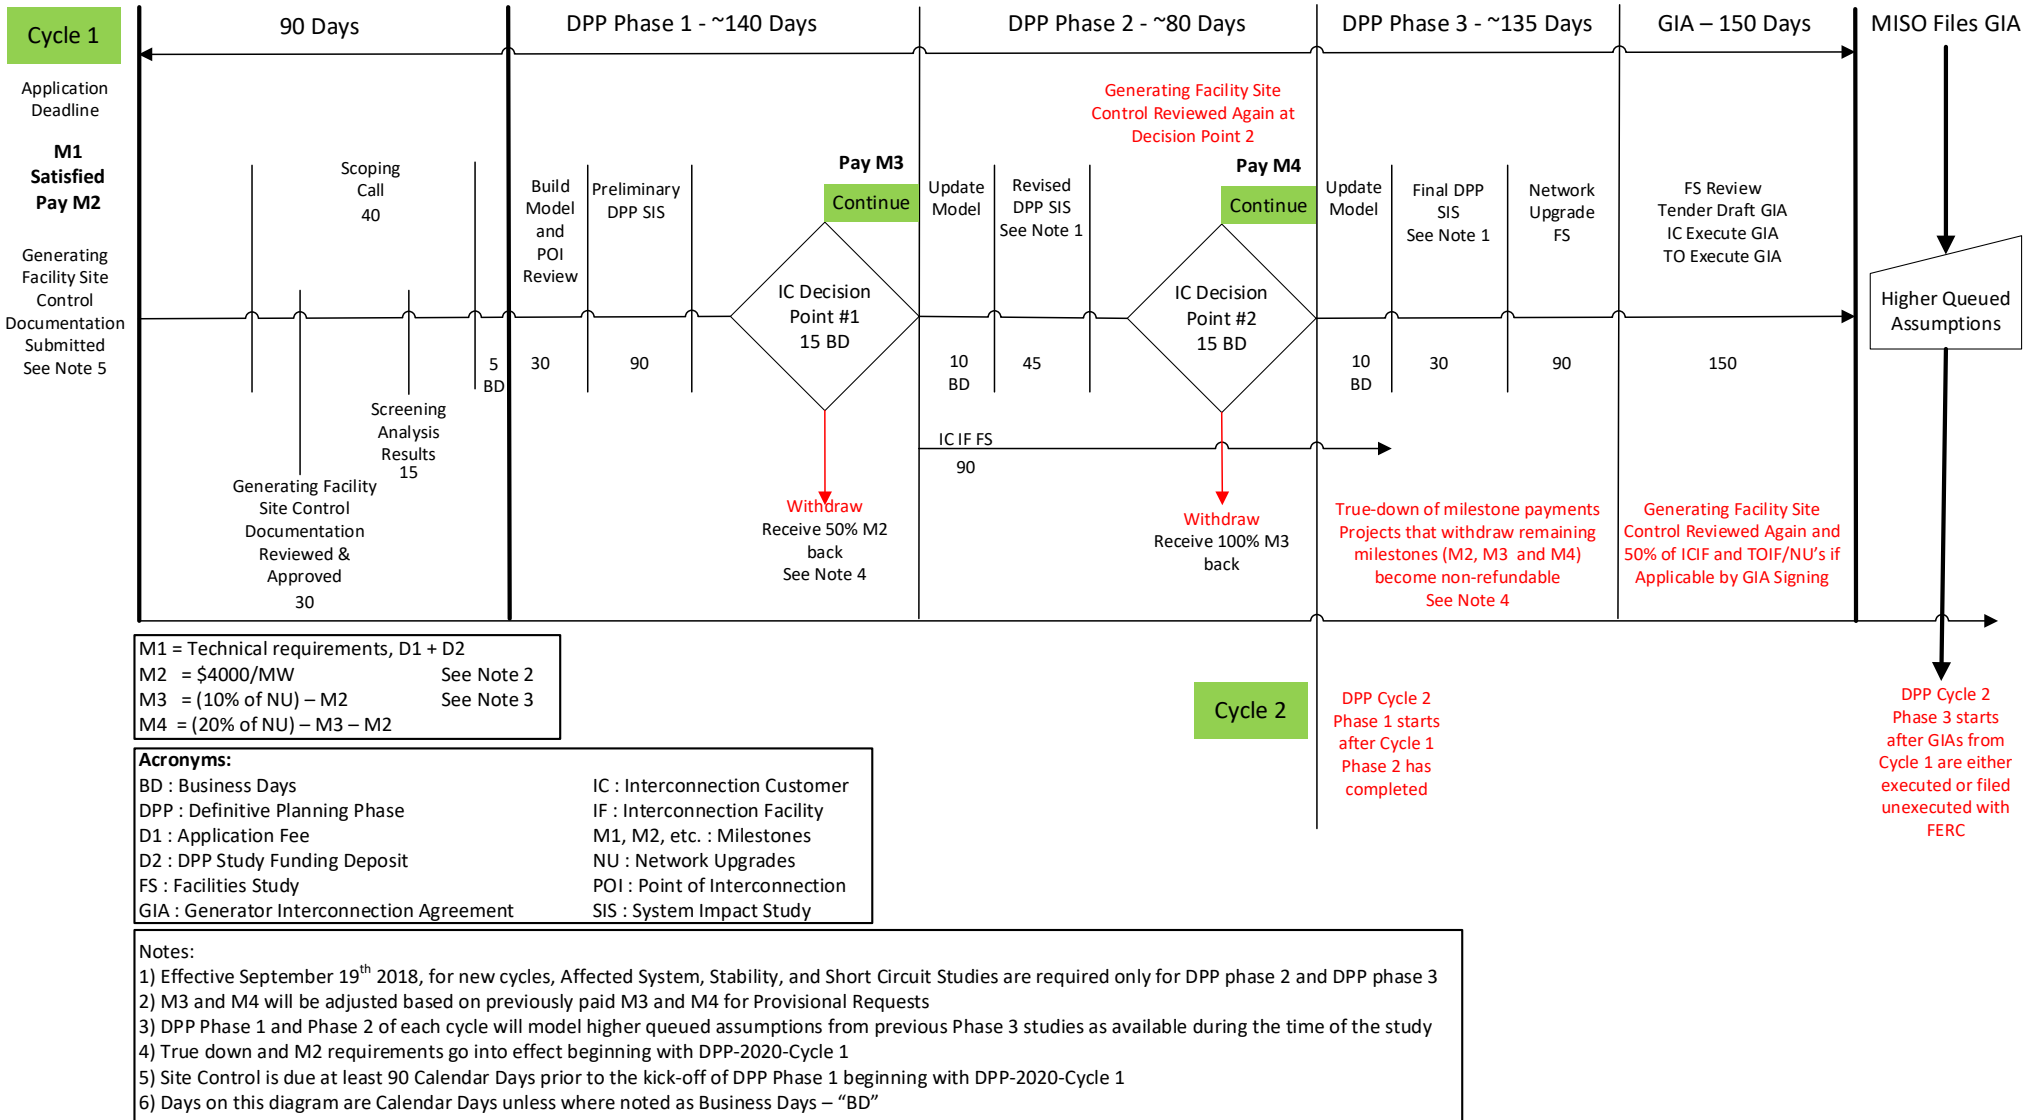

Refer to full GI Process Flow Diagram and notes for more detail: [GI Application and DPP Readiness](#)
